ARCHITECT'S FIELD REPORT

116

PROJECT	Eagle's Nest Townhouses	DATE	7/31/13
	11 Morning Glory Way & 31 Marcellina Lane		
	Mt. Crested Butte, CO 81225		

CONDITIONS			
DATE	7/31/13	TIME	3:00 pm
WEATHER	Slightly Cloudy, Warm	TEMP	73 deg

WORK OBSERVED
Phase IV Construction
TRADES PRESENT
Holgate Construction Co.

PARTIES		
Ben White	Ben White Architecture	970-349-5378
Mick Holgate	Holgate Construction Co.	970-209-4449

COMMENTS & OBSERVATIONS

- 1. Observed complete painting and belly band installation on Building E and Unit 17.
- 2. Observed work underway installing chamfer strips on the 2nd Floor Decks.
- Discussed the installation of shim strips on the top of the 3rd Floor Deck joists. The joists on this building were cut to a slope and will need to be leveled to keep the belly band straight. Crew is cutting custom shims strips out of existing deck boards.
- 4. Discussed with Mick his technique for installing address numbers.
- 5. Relayed to Mick that Units 33, 34 & 36 have requested that their existing blinds not be reinstalled.
- 6. (7) Workers were on site today, including Mick.
- 7. The project has experienced **4 days weather delay** due to snowfall on 4/9/13, 4/15/13, 5/8/13, and rain on 5/29/13.

Total Number of Construction Days – 221 Number of Construction Days to Date - 115 Percent of Construction Duration Complete – 52% Average Construction Progress Percent Complete – 47% (Reference Construction Progress Tables Below)

BEN WHITE

ARCHITECTURE

CONSTRUCTION PROGRESS

UNIT	DEMOLITION	WINDOWS & DOOR S	INTERIOR TRIM & BLINDS	PAINT CEILINGS, JOISTS ,SOFFIT	FASCIA & CHIMNEY FLASHING	BELLY BANDS AND TRIM	2 ND FLOOR MEMBRANE & SCUPPER	2 ND FLOOR DECK BOARDS	3 RD FLOOR DECK BOARDS	METAL SIDING	WOOD POST WRAPS	GUARDRAILS	LIGHT FIXTURE & OUTLET	PAINT CHIMNEY FLUES	ADDRESS NUMBERS	DAMAGES AND NOTES
17	100%	100%	0%	100%	75%	100%	0%	0%	0%	0%	0%	0%	0%	100%	0%	?
18	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	0%	1B
19	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	0%	1A,3B
20	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	0%	1A
21	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	0%	0
22	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	0%	1B
23	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	0%	1A
24	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	0%	1B,3B
25	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	0%	1A
26	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	0%	1B,3B
27	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	0%	1A
28	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	0%	1B,3B
29	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	0%	1A
30	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	0%	1B,3B
31	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	0%	0
32	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	0%	1B,3B
33	100%	100%	0%	100%	85%	100%	0%	0%	0%	0%	0%	0%	0%	100%	0%	1A,3B
34	100%	100%	0%	100%	100%	100%	0%	0%	0%	0%	0%	0%	0%	100%	0%	1A,3B
35	100%	100%	0%	100%	100%	100%	0%	0%	0%	0%	0%	0%	0%	100%	0%	0

Damage Footnotes: (A – Minor, B – Major) 1 = Degraded 2nd Floor Deck Joists, 2 = Degraded 2nd Floor Plywood Top, 3 = Degraded 3rd Floor Deck Joists



ARCHITECTURE

CONSTRUCTION PROGRESS, CONTINUED

UNIT	DEMOLITION	WINDOWS & DOOR S	INTERIOR TRIM & BLINDS	PAINT CEILINGS, JOISTS, SOFFIT	FASCIA & CHIMNEY FLASHING	BELLY BANDS AND TRIM	2 ND FLOOR MEMBRANE & SCUPPER	2 ND FLOOR DECK BOARDS	3 RD FLOOR DECK BOARDS	METAL SIDING	WOOD POST WRAPS	GUARDRAILS	LIGHT FIXTURE & OUTLET	PAINT CHIMNEY FLUES	ADDRESS NUMBERS	DAMAGES AND NOTES
36	100%	100%	0%	100%	100%	100%	0%	0%	0%	0%	0%	0%	0%	100%	0%	0
37	100%	100%	0%	100%	100%	100%	0%	0%	0%	0%	0%	0%	0%	100%	0%	1A
38	100%	100%	0%	100%	100%	100%	0%	0%	0%	0%	0%	0%	0%	100%	0%	1B,3A
39	100%	100%	0%	100%	100%	100%	25%	0%	0%	0%	0%	0%	0%	100%	0%	ЗA
40	100%	100%	0%	100%	100%	100%	25%	0%	0%	0%	0%	0%	0%	100%	0%	1B,3B
1	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	100%	0%	
2	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	100%	0%	
3	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	100%	0%	
4	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	100%	0%	
5	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	100%	0%	
6	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	100%	0%	
7	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	100%	0%	
8	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	100%	0%	
9	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	100%	0%	
10	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	100%	0%	
11	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	100%	0%	
12	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	100%	0%	
13	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	100%	0%	
14	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	100%	0%	
15	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	100%	0%	
16	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	100%	0%	

BEN WHITE

ARCHITECTURE

MATERIAL STATUS SUMMARY

REVISED 6/12/13

MATERIAL	MANUFACTURER	STATUS
Metal Siding "Sage"	Emco Building	100% Ordered
	Products, Inc.	Materials on Site
Metal Siding "Royal Brown"	Emco Building	100% Ordered
	Products, Inc.	Materials on Site
Metal Corner Trim "Sage"	Emco Building	100% Ordered
-	Products, Inc.	Materials on Site
Metal Corner Trim "Sage"	Emco Building	100% Ordered
at revised 9'-4" length	Products, Inc.	Materials on Site
Standing Seam Wall Panels	Dragon Sheet	Not Ordered
	Metal	Materials Available Locally
EPDM Deck Membrane	Carlisle Syntec	60% Ordered
	45 mil EPDM	Materials Available Locally
Chimney Flue Paint "Black"	Rustoleum 1200	100% Ordered
	Degree Enamel	Available Locally
Ceiling, Joist, Soffit Paint	Sherwin Williams	Paint available locally.
	"Spalding Gray"	
Trim, Belly Bands, & Fascia	MiraTec with SW	80% Ordered
	"ENT Brown"	Materials on Site
Doors and Windows	Eagle Windows	100% Ordered
	& Doors	Materials on Site
Door Hardware	Eagle Doors	Hardware is shipped with the doors.
Revised Hardware	Eagle Doors	Order Pending Restock Fees
	0	(40) Door and Buildings C & D
Wood Column Wraps	MiraTec with SW	60% Ordered
	"ENT Brown"	Materials on Site
Metal Guardrails	Fortress Fe26	100% Ordered
	"Flat Black"	Materials on Site
Exterior Light Fixtures	World Imports	100% Ordered
-	Essen	Materials On Site
Outlet Covers	By CBL	40% Complete
		Installation by CBL
Scupper Drains	Dragon Sheet	40% Ordered
	Metal	Materials Available Locally
Address Numbers	Architectural	Type and Quantity to MH
	Mailboxes	Order Placed, Pending Arrival
Deck Boards	Fiberon	60% Ordered
		Material on Site
Light Bulbs	9W CFL	100% Ordered
		Materials on Site

BEN WHITE

ARCHITECTURE

CONSTRUCTION SCHEDULE

REVISED 7/31/13


BUILDING & UNIT	WEEK BEFORE	START DATE	FINISH DATE	WEEK AFTER
Building C				
18	N/A	4/8/13	6/14/13	6/21/13
19 & 20	N/A	4/8/13	6/14/13	6/21/13
21 & 22	N/A	4/8/13	6/14/13	6/21/13
23 & 24	N/A	4/8/13	6/14/13	6/21/13
Building D				
25 & 26	N/A	4/24/13	6/21/13	6/28/13
27 & 28	N/A	4/24/13	6/21/13	6/28/13
29 & 30	N/A	4/24/13	6/21/13	6/28/13
31 & 32	N/A	4/24/13	6/21/13	6/28/13
Building E				
33 & 34	6/17/13	6/24/13	8/23/13	8/30/13
35 & 36	6/17/13	6/24/13	8/23/13	8/30/13
Week of July 4th		7/1/13	7/5/13	
Week of Aug 5th		8/5/13	8/9/13	
37 & 38	6/17/13	6/24/13	8/23/13	8/30/13
39 & 40	6/17/13	6/24/13	8/23/13	8/30/13
Building B				
9 & 10	8/19/13	8/26/13	9/4/13	9/11/13
11 & 12	8/19/13	8/26/13	9/4/13	9/11/13
13 & 14	8/19/13	8/26/13	9/4/13	9/11/13
15 & 16	8/19/13	8/26/13	9/4/13	9/11/13
Unit 17				
17	N/A	7/8/13	8/23/13	8/30/13
Building A				
1 & 2	9/30/13	10/7/13	11/15/13	11/22/13
3 & 4	9/30/13	10/7/13	11/15/13	11/22/13
5&6	9/30/13	10/7/13	11/15/13	11/22/13
7 & 8	9/30/13	10/7/13	11/15/13	11/22/13
Total Construction			221	Days

PHOTO -WORK ITEM DESCRIPTION ACTION 7/31/13 – Photo Note Lower Level Building E View from below. Note 7/31/13 – Photo Building E Construction Looking South Ceiling, Joist and Soffit paint is complete. Belly Band is installed and scupper cut-out are complete. 7/31/13 - Photo Note South Work Area Dumpster has been removed. 7/31/13 – Photo Note Lower Level Looking North

WHITE

ARCHITECTURE

BEN

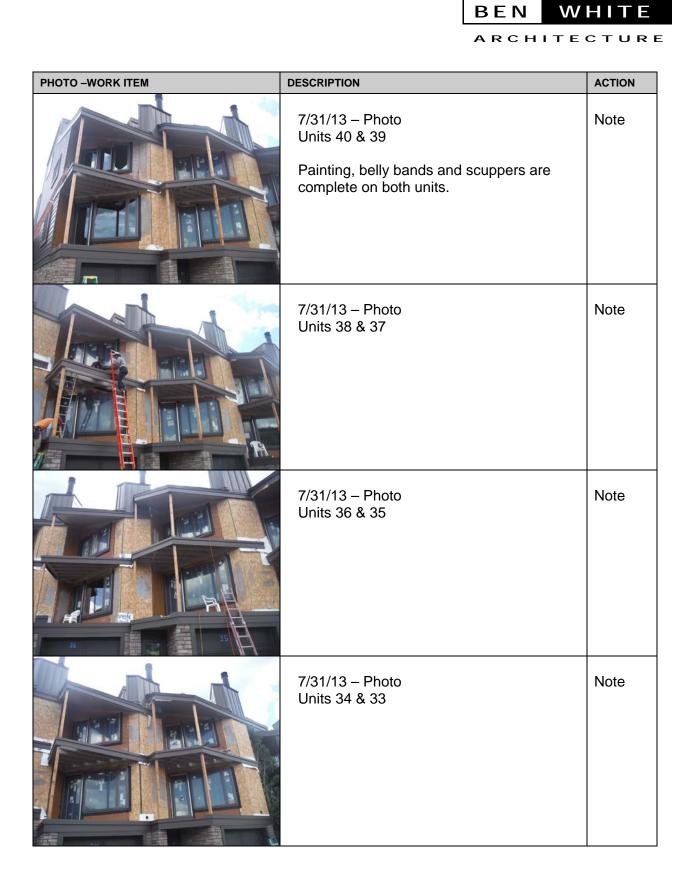



BEN

WHITE

PHOTO -WORK ITEM DESCRIPTION ACTION 7/31/13 – Photo Note Unit 35 Door Pan Flashing Bituthene pan flashing has been installed at all door thresholds. 7/31/13 – Photo Note Deck Shims for 3rd Floor Decks Deck joists on Building E were cut to a slope for drainage. This condition is unique to Building E. The crew is working on cutting shims to level the Fiberon deck boards. 7/31/13 – Photo Note Deck Shims at Unit 38 Shim strips in place. 7/31/13 – Photo Note Lot Between Units 33 & 32 Landscaping work performed by Crested Butte Lodging.

END OF FIELD REPORT

WHITE

ARCHITECTURE

BEN
